ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Predecessors	% Complete	Actual Start	Actual Finish	Remaining Duration	Fixed Cost
1		**Automotive Production Line Expansion**	**198 days**	**Tue 9/1/26**	**Thu 6/3/27**	**Tue 9/1/26**	**Thu 6/3/27**		**16%**	**Tue 9/1/26**	**NA**	**165.51 days**	**$0**
2		**Project Management**	**75 days**	**Tue 9/1/26**	**Mon 12/14/2**	**Tue 9/1/26**	**Mon 12/14/2**		**45%**	**Tue 9/1/26**	**NA**	**41.19 days**	**$0**
3		Project Kick-off	4 days	Tue 9/1/26	Thu 9/3/26	Tue 9/1/26	Tue 9/22/26		75%	Tue 9/1/26	NA	1 day	$30,200
4	✓	Project Charter Preparation	2 days	Fri 9/4/26	Mon 9/7/26	Fri 9/4/26	Mon 9/7/26	3	100%	Fri 9/4/26	Mon 9/7/26	0 days	$34,400
5		Master Schedule Developmer	34 days	Tue 9/8/26	Fri 10/23/26	Tue 9/8/26	Fri 10/23/26	4	65%	Tue 9/8/26	NA	11.9 days	$49,800
6		Cost Baseline Development	4 days	Mon 10/26/2	Thu 10/29/26	Mon 10/26/2	Thu 10/29/26	5	0%	NA	NA	4 days	$50,600
7		Weekly Progress Monitoring	72 days	Fri 9/4/26	Mon 12/14/2	Fri 9/4/26	Mon 12/14/2	3	35%	Fri 9/4/26	NA	46.8 days	$203,500
8		**Engineering & Design**	**50 days**	**Tue 9/8/26**	**Mon 11/16/2**	**Tue 9/8/26**	**Mon 11/16/2**		**21%**	**Tue 9/8/26**	**NA**	**39.45 days**	**$0**
9		Process Requirements	18 days	Tue 9/8/26	Thu 10/1/26	Tue 9/8/26	Thu 10/1/26	4	75%	Tue 9/8/26	NA	4.5 days	$54,800
10		Production Process Analysis	6 days	Fri 10/2/26	Fri 10/9/26	Fri 10/2/26	Fri 10/9/26	9	0%	NA	NA	6 days	$62,400
11		Line Concept Design	8 days	Mon 10/12/2	Wed 10/21/2	Mon 10/12/2	Wed 10/21/2	10	0%	NA	NA	8 days	$42,500
12		Equipment Specifications	6 days	Thu 10/22/26	Thu 10/29/26	Thu 10/22/26	Thu 10/29/26	11	0%	NA	NA	6 days	$45,600
13		Mechanical Design	10 days	Fri 10/30/26	Thu 11/12/26	Fri 10/30/26	Thu 11/12/26	12	0%	NA	NA	10 days	$62,800
14		Electrical Design	8 days	Fri 10/30/26	Tue 11/10/26	Fri 10/30/26	Tue 11/10/26	12	0%	NA	NA	8 days	$42,500
15		Automation Architecture	6 days	Fri 10/30/26	Fri 11/6/26	Fri 10/30/26	Fri 11/6/26	12	0%	NA	NA	6 days	$47,400
16		Design Approval	2 days	Fri 11/13/26	Mon 11/16/2	Fri 11/13/26	Mon 11/16/2	13,14,15	0%	NA	NA	2 days	$55,400
17		**Procurement**	**50 days**	**Tue 11/17/26**	**Mon 1/25/27**	**Tue 11/17/26**	**Mon 1/25/27**		**0%**	**NA**	**NA**	**50 days**	**$0**
18		RFQ Preparation	4 days	Tue 11/17/26	Fri 11/20/26	Tue 11/17/26	Fri 11/20/26	16	0%	NA	NA	4 days	$33,800
19		RFQ Issuance	4 days	Mon 11/23/2	Thu 11/26/26	Mon 11/23/2	Thu 11/26/26	18	0%	NA	NA	4 days	$32,700
20		Technical Bid Evaluation	6 days	Fri 11/27/26	Fri 12/4/26	Fri 11/27/26	Fri 12/4/26	19	0%	NA	NA	6 days	$47,400
21		Supplier Evaluation	4 days	Mon 12/7/26	Thu 12/10/26	Mon 12/7/26	Thu 12/10/26	20	0%	NA	NA	4 days	$50,600
22		Contract Negotiation	6 days	Thu 12/10/26	Thu 12/17/26	Thu 12/10/26	Thu 12/17/26	21FS-1 day	0%	NA	NA	6 days	$58,200
23		Robot Cell Manufacturing	24 days	Thu 12/17/26	Tue 1/19/27	Thu 12/17/26	Tue 1/19/27	22FS-1 day	0%	NA	NA	24 days	$81,700
24		Conveyor Manufacturing	20 days	Thu 12/17/26	Wed 1/13/27	Thu 12/17/26	Wed 1/13/27	22FS-1 day	0%	NA	NA	20 days	$85,600
25		Equipment Delivery & Inspect	4 days	Wed 1/20/27	Mon 1/25/27	Wed 1/20/27	Mon 1/25/27	23,24	0%	NA	NA	4 days	$47,000
26		**Site Preparation & Installation**	**65 days**	**Mon 11/16/2**	**Fri 2/12/27**	**Mon 11/16/2**	**Fri 2/12/27**		**0%**	**NA**	**NA**	**65 days**	**$0**
27		Site Survey	2 days	Mon 11/16/2	Tue 11/17/26	Mon 11/16/2	Tue 11/17/26	16FS-1 day	0%	NA	NA	2 days	$51,200
28		Site Preparation	6 days	Tue 11/17/26	Tue 11/24/26	Tue 11/17/26	Tue 11/24/26	27FS-1 day	0%	NA	NA	6 days	$62,400
29		Foundation Preparation	6 days	Tue 11/24/26	Tue 12/1/26	Tue 11/24/26	Tue 12/1/26	28FS-1 day	0%	NA	NA	6 days	$39,000
30		Mechanical Equipment Installation	8 days	Wed 1/20/27	Fri 1/29/27	Wed 1/20/27	Fri 1/29/27	25SS,29FS-1 day	0%	NA	NA	8 days	$50,900
31		Power Cable Installation	8 days	Fri 1/29/27	Tue 2/9/27	Fri 1/29/27	Tue 2/9/27	30FS-1 day	0%	NA	NA	8 days	$63,500
32		Robot Cell Installation	6 days	Fri 1/29/27	Fri 2/5/27	Fri 1/29/27	Fri 2/5/27	30FS-1 day	0%	NA	NA	6 days	$43,200
33		Conveyor Installation	6 days	Fri 1/29/27	Fri 2/5/27	Fri 1/29/27	Fri 2/5/27	30FS-1 day	0%	NA	NA	6 days	$47,400
34		Utility Connections	4 days	Tue 2/9/27	Fri 2/12/27	Tue 2/9/27	Fri 2/12/27	31FS-1 day,32FS-	0%	NA	NA	4 days	$54,800
35		**Automation & Integration**	**29 days**	**Mon 2/8/27**	**Thu 3/18/27**	**Mon 2/8/27**	**Thu 3/18/27**		**0%**	**NA**	**NA**	**29 days**	**$0**
36		PLC Panel Installation	4 days	Mon 2/15/27	Thu 2/18/27	Mon 2/15/27	Thu 2/18/27	34	0%	NA	NA	4 days	$59,000
37		PLC Hardware Configuration	4 days	Fri 2/19/27	Wed 2/24/27	Fri 2/19/27	Wed 2/24/27	36	0%	NA	NA	4 days	$33,800
38		PLC Programming	10 days	Thu 2/25/27	Wed 3/10/27	Thu 2/25/27	Wed 3/10/27	37	0%	NA	NA	10 days	$50,200
39		Robot Programming	10 days	Mon 2/8/27	Fri 2/19/27	Mon 2/8/27	Fri 2/19/27	32	0%	NA	NA	10 days	$54,400

Project: Saipa_Diesel_Construction_Project 3
Date: Sun 10/11/26


Task	Inactive Task	Manual Summary Rollup	External Milestone	Manual Progress
Split	Inactive Milestone	Manual Summary	Deadline	
Milestone	Inactive Summary	Start-only	Critical	
Summary	Manual Task	Finish-only	Critical Split	
Project Summary	Duration-only	External Tasks	Progress	

ID	Task Mode	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Predecessors	% Complete	Actual Start	Actual Finish	Remaining Duration	Fixed Cost
40		MES Interface Development	8 days	Thu 2/25/27	Mon 3/8/27	Thu 2/25/27	Mon 3/8/27	38SS	0%	NA	NA	8 days	$59,300
41		Safety PLC Programming	6 days	Thu 2/25/27	Thu 3/4/27	Thu 2/25/27	Thu 3/4/27	37	0%	NA	NA	6 days	$62,400
42		Full Line Integration	6 days	Thu 3/11/27	Thu 3/18/27	Thu 3/11/27	Thu 3/18/27	38,39,40,41	0%	NA	NA	6 days	$51,600
43		**Testing & Commissioning**	**29 days**	**Fri 3/19/27**	**Wed 4/28/27**	**Fri 3/19/27**	**Wed 4/28/27**		**0%**	**NA**	**NA**	**29 days**	**$0**
44		Pre-Commissioning Inspectior	3 days	Fri 3/19/27	Tue 3/23/27	Fri 3/19/27	Tue 3/23/27	42	0%	NA	NA	3 days	$48,800
45		Dry Run	4 days	Wed 3/24/27	Mon 3/29/27	Wed 3/24/27	Mon 3/29/27	44	0%	NA	NA	4 days	$59,000
46		Functional Test	4 days	Tue 3/30/27	Fri 4/2/27	Tue 3/30/27	Fri 4/2/27	45	0%	NA	NA	4 days	$33,800
47		Safety System Validation	4 days	Mon 4/5/27	Thu 4/8/27	Mon 4/5/27	Thu 4/8/27	46	0%	NA	NA	4 days	$38,000
48		Cycle Time Measurement	4 days	Fri 4/9/27	Wed 4/14/27	Fri 4/9/27	Wed 4/14/27	47	0%	NA	NA	4 days	$46,400
49		Product Quality Validation	6 days	Thu 4/15/27	Thu 4/22/27	Thu 4/15/27	Thu 4/22/27	48	0%	NA	NA	6 days	$58,200
50		Run-at-Rate Test	4 days	Fri 4/23/27	Wed 4/28/27	Fri 4/23/27	Wed 4/28/27	49	0%	NA	NA	4 days	$38,000
51		**Handover & Closeout**	**26 days**	**Thu 4/29/27**	**Thu 6/3/27**	**Thu 4/29/27**	**Thu 6/3/27**		**0%**	**NA**	**NA**	**26 days**	**$0**
52		Pilot Production Preparation	4 days	Thu 4/29/27	Tue 5/4/27	Thu 4/29/27	Tue 5/4/27	50	0%	NA	NA	4 days	$42,200
53		Pilot Production Run	7 days	Wed 5/5/27	Thu 5/13/27	Wed 5/5/27	Thu 5/13/27	52	0%	NA	NA	7 days	$49,800
54		Pilot Quality Inspection	5 days	Fri 5/14/27	Thu 5/20/27	Fri 5/14/27	Thu 5/20/27	53	0%	NA	NA	5 days	$50,600
55		Final Performance Verificatior	5 days	Fri 5/21/27	Thu 5/27/27	Fri 5/21/27	Thu 5/27/27	54	0%	NA	NA	5 days	$59,000
56		System Handover	3 days	Fri 5/28/27	Tue 6/1/27	Fri 5/28/27	Tue 6/1/27	55	0%	NA	NA	3 days	$42,800
57		Project Closeout	2 days	Wed 6/2/27	Thu 6/3/27	Wed 6/2/27	Thu 6/3/27	56	0%	NA	NA	2 days	$53,700

Project: Saipa_Diesel_Construction_Project 3
Date: Sun 10/11/26

Task	Inactive Task	Manual Summary Rollup	External Milestone	Manual Progress	
Split	Inactive Milestone	Manual Summary	Deadline		
Milestone	Inactive Summary	Start-only	Critical		
Summary	Manual Task	Finish-only	Critical Split		
Project Summary	Duration-only	External Tasks	Progress		

Baseline Cost
$2,622,300
$368,500
$30,200
$34,400
$49,800
$50,600
$203,500
$413,400
$54,800
$62,400
$42,500
$45,600
$62,800
$42,500
$47,400
$55,400
$437,000
$33,800
$32,700
$47,400
$50,600
$58,200
$81,700
$85,600
$47,000
$412,400
$51,200
$62,400
$39,000
$50,900
$63,500
$43,200
$47,400
$54,800
$370,700
$59,000
$33,800
$50,200
$54,400

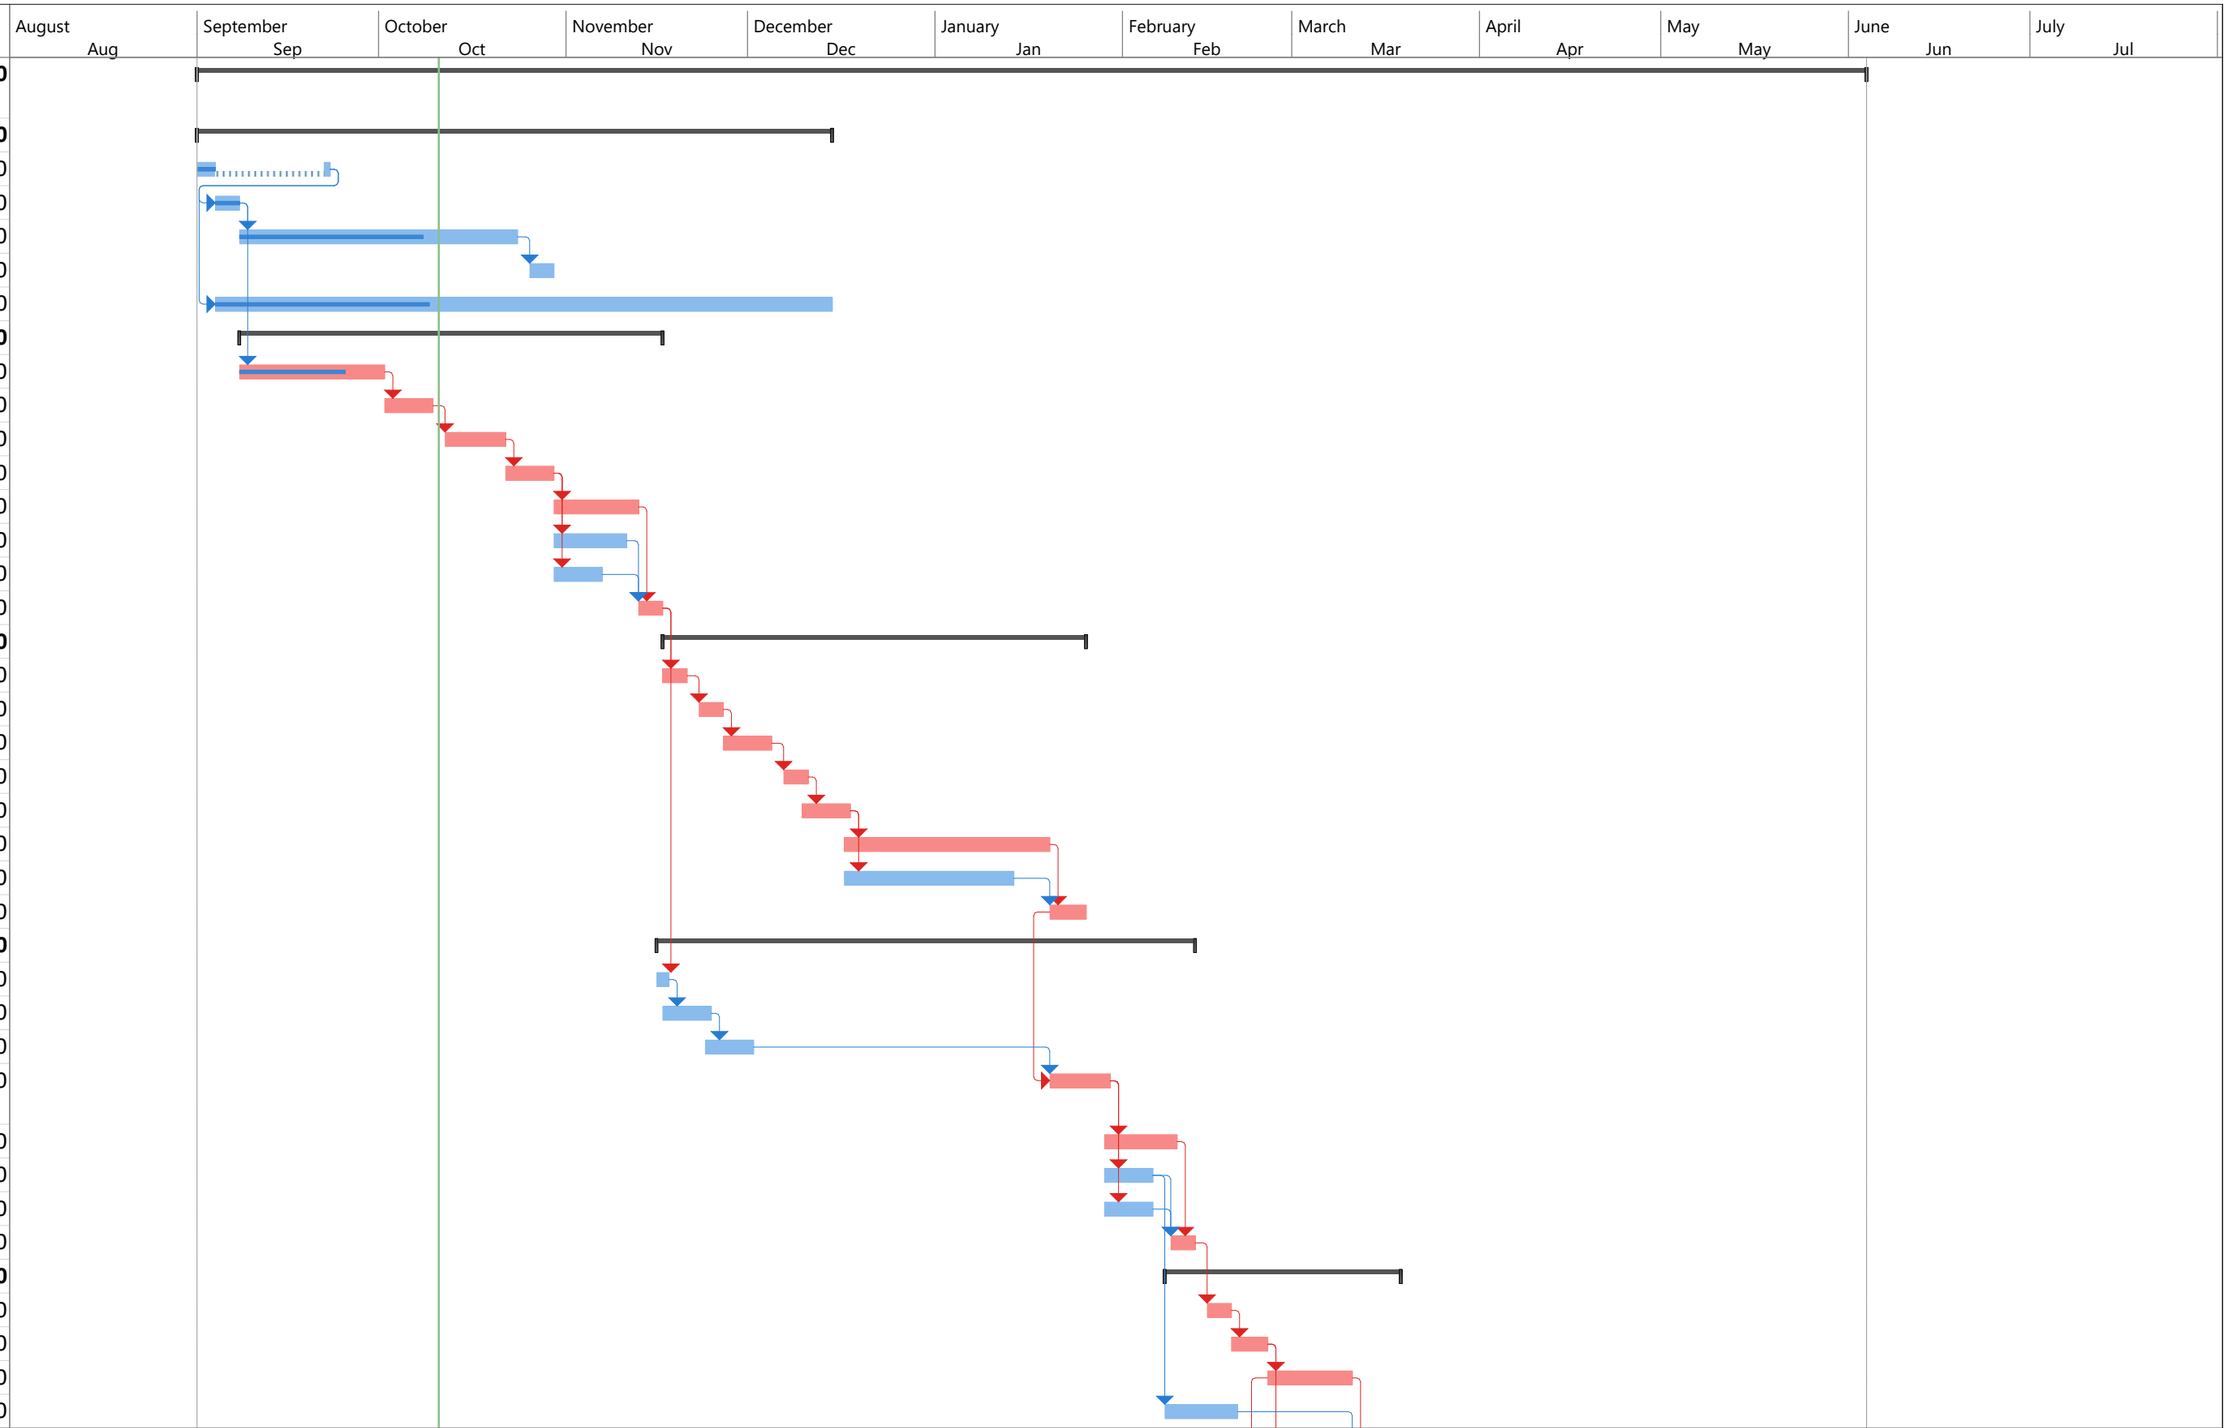

Project: Saipa_Diesel_Construction_Project 3
Date: Sun 10/11/26

Task	Inactive Task	Manual Summary Rollup	External Milestone	Manual Progress
Split	Inactive Milestone	Manual Summary	Deadline	
Milestone	Inactive Summary	Start-only	Critical	
Summary	Manual Task	Finish-only	Critical Split	
Project Summary	Duration-only	External Tasks	Progress	

Baseline Cost	August Aug	September Sep	October Oct	November Nov	December Dec	January Jan	February Feb	March Mar	April Apr	May May	June Jun	July Jul
$59,300												
$62,400												
$51,600												
$322,200												
$48,800												
$59,000												
$33,800												
$38,000												
$46,400												
$58,200												
$38,000												
$298,100												
$42,200												
$49,800												
$50,600												
$59,000												
$42,800												
$53,700												

Project: Saipa_Diesel_Construction_Project 3
Date: Sun 10/11/26

Task	Inactive Task	Manual Summary Rollup	External Milestone	Manual Progress	
Split	Inactive Milestone	Manual Summary	Deadline		
Milestone	Inactive Summary	Start-only	Critical		
Summary	Manual Task	Finish-only	Critical Split		
Project Summary	Duration-only	External Tasks	Progress		
